

# Space and Missile Systems Center



## GPS Control Segment

Luke J. Schaub  
Chief, GPS Control Segment Division  
29 Apr 15

Report Documentation Page				Form Approved OMB No. 0704-0188	
Public reporting burden for the collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302. Respondents should be aware that notwithstanding any other provision of law, no person shall be subject to a penalty for failing to comply with a collection of information if it does not display a currently valid OMB control number.					
1. REPORT DATE <b>29 APR 2015</b>		2. REPORT TYPE		3. DATES COVERED <b>00-00-2015 to 00-00-2015</b>	
4. TITLE AND SUBTITLE <b>GPS Control Segment</b>				5a. CONTRACT NUMBER	
				5b. GRANT NUMBER	
				5c. PROGRAM ELEMENT NUMBER	
6. AUTHOR(S)				5d. PROJECT NUMBER	
				5e. TASK NUMBER	
				5f. WORK UNIT NUMBER	
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) <b>Air Force Space Command, Space and Missile Systems Center, GPS Control Segment Division, Los Angeles AFB, El Segundo, CA, 90245</b>				8. PERFORMING ORGANIZATION REPORT NUMBER	
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)				10. SPONSOR/MONITOR'S ACRONYM(S)	
				11. SPONSOR/MONITOR'S REPORT NUMBER(S)	
12. DISTRIBUTION/AVAILABILITY STATEMENT <b>Approved for public release; distribution unlimited</b>					
13. SUPPLEMENTARY NOTES <b>Presented at the GPS Partnership Council 2015 (GPSPC15), held April 29 to May 1, 2015, at the Los Angeles AFB, CA.</b>					
14. ABSTRACT					
15. SUBJECT TERMS					
16. SECURITY CLASSIFICATION OF:			17. LIMITATION OF ABSTRACT <b>Same as Report (SAR)</b>	18. NUMBER OF PAGES <b>12</b>	19a. NAME OF RESPONSIBLE PERSON
a REPORT <b>unclassified</b>	b ABSTRACT <b>unclassified</b>	c THIS PAGE <b>unclassified</b>			




# Agenda

*SPACE AND MISSILE SYSTEMS CENTER*

- Next Generation Operational Control System (OCX)
- Contingency Operations

# OCX Overview

## SPACE AND MISSILE SYSTEMS CENTER

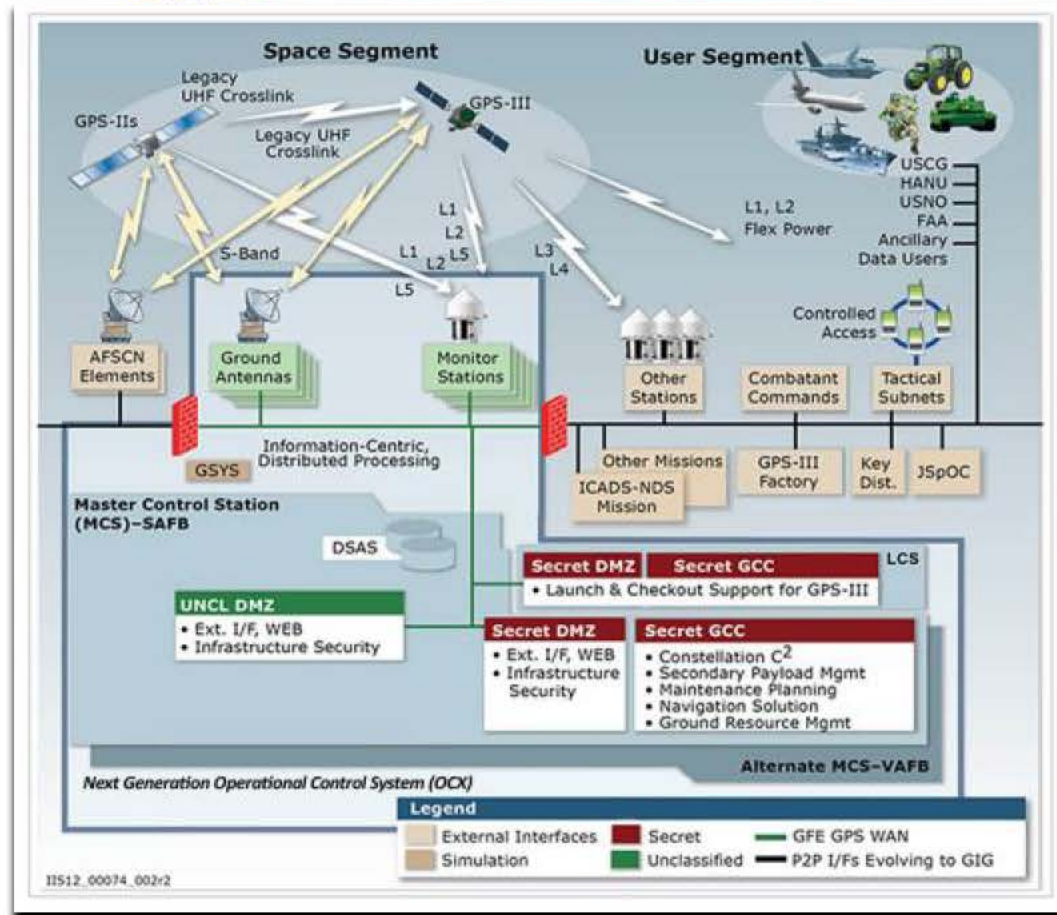

- Master/Alternate Control Stations
  - Launch and Checkout System (LCS)
    - Launch and Checkout of GPS IIIs
    - Command & Control (C2) for GPS IIIs in launch / checkout
  - Mission Planning & Scheduling
  - Mission Situational Awareness
  - Constellation & Satellite C2
  - Position, Navigation, and Timing
  - Integrity & Continuity Assurance
- Global Monitoring Station Network
  - 17 globally dispersed sites
  - Monitor quality of broadcast signals and provide input to navigation solution
- Legacy Ground Antennas (LGAs)
  - 4 globally dispersed sites
  - Support data links and signals between the ground and space vehicles
- GPS System Simulator (GSYS)
  - Test driver and anomaly resolution

### Acronyms

AFSCN: Air Force Satellite Control Network  
 DMZ: De-militarized Zone  
 DSAS: Data Storage and Analysis System  
 FAA: Federal Aviation Administration  
 GCC: GPS Control Center

GFE: Government Furnished Equipment  
 GIG: Global Information Grid  
 GPS: Global Positioning System  
 HANU: High Accuracy Navigation User  
 I/F: Interface

ICADS: Integration & Correlation Display System  
 MCS: Master Control Station  
 Mgmt: Management  
 NDS: Nuclear Detection System  
 P2P: Point-to-point

SAFB: Schriever Air Force Base  
 UHF: Ultra-High Frequency  
 USCG: U.S. Coast Guard  
 VAFB: Vandenberg Air Force Base  
 WAN: Wide-area Network





# Block 0 Accomplishment/Status

*SPACE AND MISSILE SYSTEMS CENTER*

- ✓ Block 0 (Launch & Checkout System, LCS) Baseline Integrated, Jun 2014
- ✓ LCS Launch Exercise 4, Oct 2014
- ✓ LCS Configuration Item Qualification Test Procedures (126)  
First Dry Run, Dec 2014
- ✓ LCS Consent to Ship, Apr 2015
- ☐ Schriever AFB Equipment Installed, May 2015
- ☐ LCS Configuration Item Qualification Test, Jul 2015
- ☐ Final LCS Hardware/Software Sell-off, Nov 2015
- ☐ LCS Site Acceptance Test, Mar 2016



# Block 1 Accomplishments/Status

*SPACE AND MISSILE SYSTEMS CENTER*

- ✓ Block 1 Strategic Pause, Dec 2013
  - Root cause and corrective action identification
  - Over-Target-Baseline foundations
- ✓ Iteration 1.6 Segment Design Walkthrough, Jan 2015
  - Requirements flow-down established for all configuration Items
- ✓ Segment/Element Engineering Freeze Review, Jan 2015
  - 13-month effort to re-baseline Block 1 systems engineering
- ☐ Iteration 1.6 Preliminary Design Walkthrough, May 2015
  - Nearing completion, leads to detailed design activities
- ☐ Iteration 1.6 Critical Design Review, Jul 2015
  - Culmination of detailed design leads to code and unit test activities
- ☐ Iteration 1.7 Segment Design Walkthrough, Nov 2015
  - Establishes requirements flow-down for all configuration Items





# Recent Program Activities

*SPACE AND MISSILE SYSTEMS CENTER*

- Rebaselined Program:
  - Over Target Baseline (OTB), Jul 2014
  - AF Service Cost Position (SCP), Nov 2014
  - Block 0 (LCS) acceptance now May 2016
  - Block 1 (with core M-Code) Ready for Transition to Operations (RTO) in Jul 2019
- AT&L Deep Dive held with Mr Kendall, Feb 2015
  - Air Force and Raytheon detailed cost, schedule and performance assessments
  - Established Cost/Schedule Tripwires against SCP baseline
  - Implement GPS III Contingency Operations



# Why Contingency Operations?

*SPACE AND MISSILE SYSTEMS CENTER*

- GPS III SV01 needed operational by Sep 2019
- GPS III healthy operations dependent on delivery of OCX Block 1
  - Current control system cannot fly the GPS III
- OCX schedule puts constellation sustainment at risk
  - Jul 2019 projected OCX RTO






# What is Contingency Operations?

*SPACE AND MISSILE SYSTEMS CENTER*

- Provides GPS III SV command and control
- NAV capability equivalent to GPS IIF (legacy and modern signals)
  - No L1C or GPS III enhanced message types
  - No modern signal monitoring until OCX Block 1
- Includes the Nuclear Detonation Detection System (NDS)
- Requires delivery of OCX Block 0 for launch


# Contingency Ops Architecture (Notional)

SPACE AND MISSILE SYSTEMS CENTER

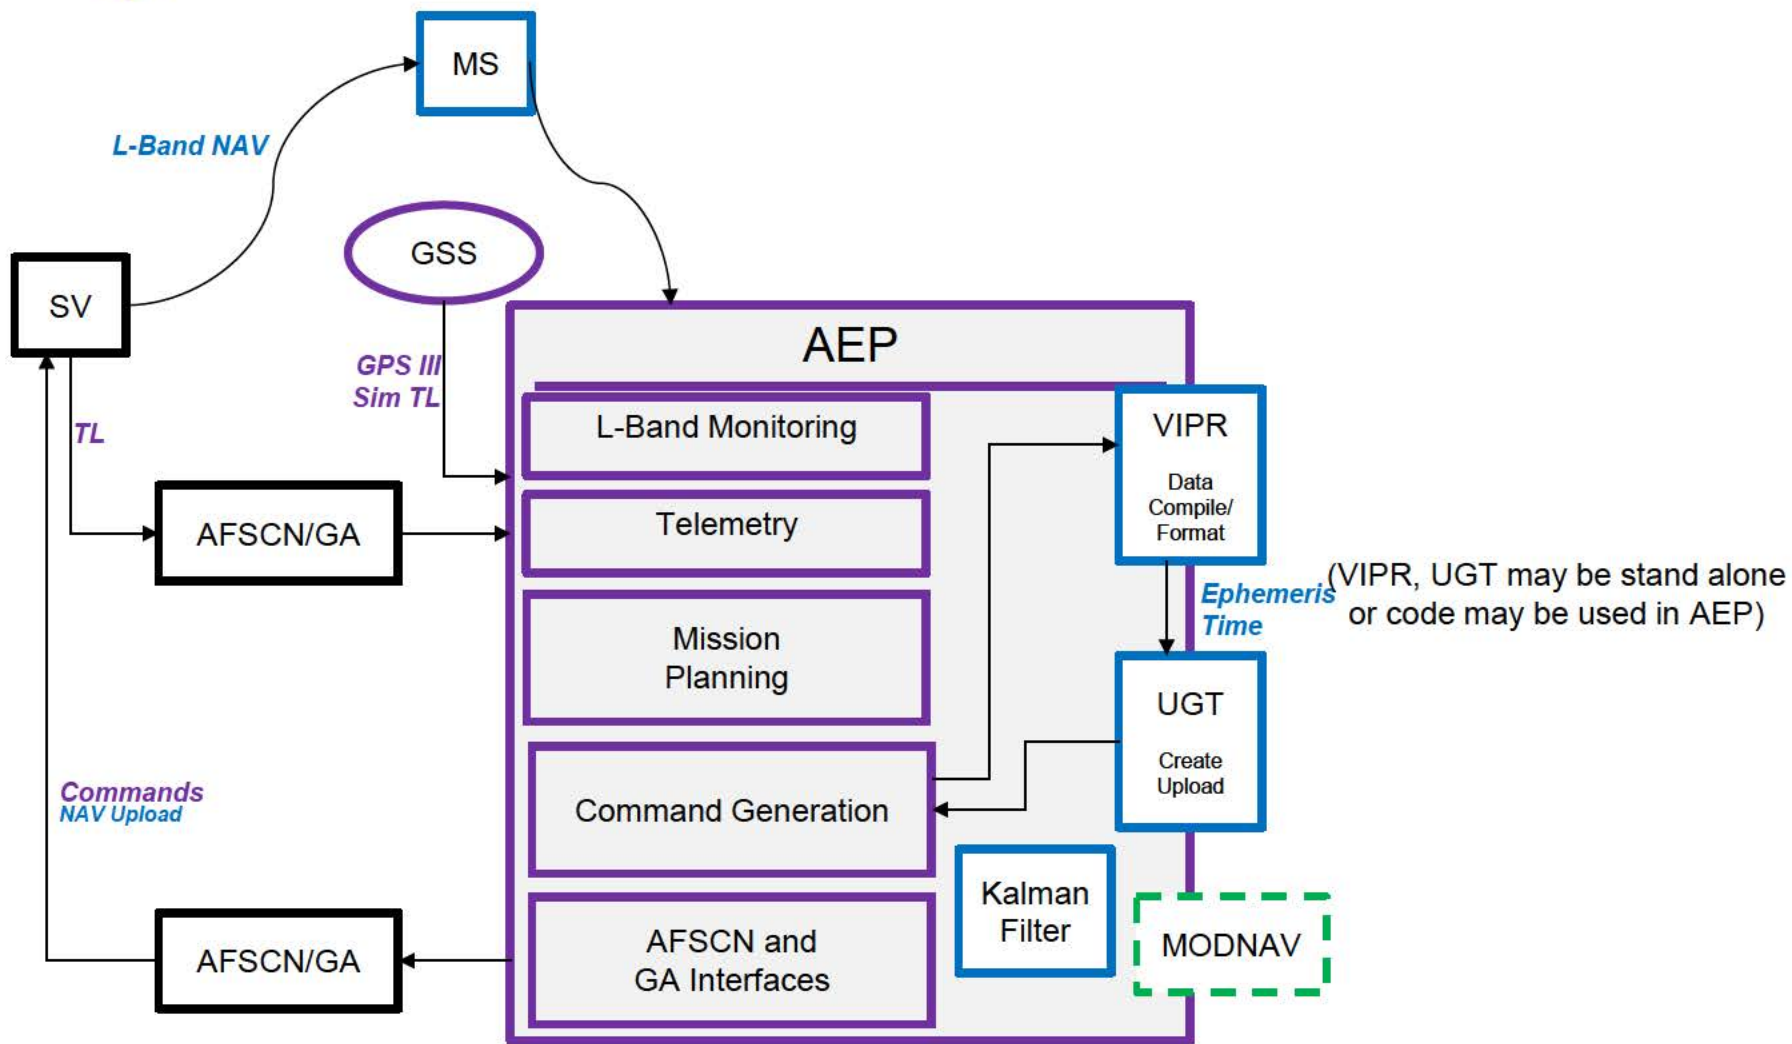



## SPACE AND MISSILE SYSTEMS CENTER







# Contingency Ops Status & Way Ahead

*SPACE AND MISSILE SYSTEMS CENTER*

- ✓ 5 Feb – Air Force decision to implement
- ✓ 15 Mar – Phase 2 Special Study RFP
- ☐ Jun 15 – Phase 2 Study Authority To Proceed (ATP)
- ☐ Jun 15 – Implementation RFP
- ☐ Jan 16 – Implementation ATP
- ☐ Apr 19 – Ready for Transition to Operations



# Summary

*SPACE AND MISSILE SYSTEMS CENTER*

- OCX: Two steps forward, one step back
- Contingency Operations: Full speed ahead
